Community High School District 99

Master Facility Plan Implementation

Weekly Construction Progress Report

Period: 5/21/20 - 6/04/20

Wight Construction Services
2500 North Frontage Road
Darien, IL 60561

Downers Grove South High School

Phase B - Fine Arts Addition

- Continued framing guardrail toe kick & taping of demo kitchen area
- Continued installing casework at 2nd floor
- Installed outside wood grain soffit panels. Started pouring floor prep for ceramic tile
- Started hanging light fixtures on 2nd floor. Continued trimming out outlets
- Finished painting 2nd floor classroom walls/ceilings & started painting 2nd floor corridor
- Pulled fire alarm cable on first floor classrooms

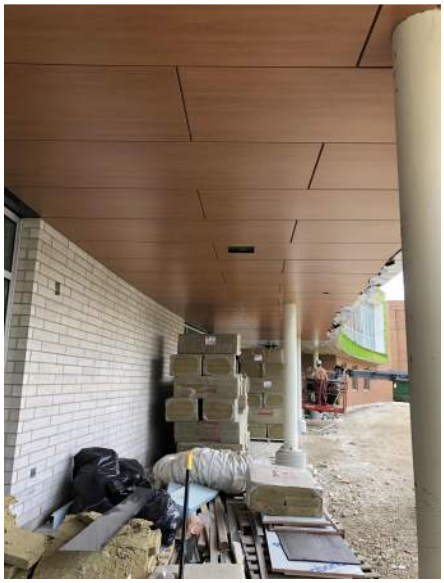

360° Pictures: Demo Kitchen | 1st Floor Art Gallery | 2nd Floor Classroom | Jewelry/2D Studio

Downers Grove South High School

Phase B - Bleachers & Squad Rooms

- Started installing masonry walls
- Started installing metal framing/siding
- Started pulling fiber to press box
- Started installing electrical power & lighting rough in

Downers Grove South High School

Phase C - Auditorium

- Started excavations of lower level footings including mat foundations & elevator pit
- Excavations above were followed by forming basement fittings & rebar
- Poured South East foundations of Auditorium
- Drilled holes in North Wall and installed corresponding rebar following changes due to existing conditions

Downers Grove South High School

Phase C - Learning Commons

- Started demo and abatement of courtyard windows on West and South elevations followed by brick and block demo followed by temp walls installation at openings
- Poured commons SOG
- Completed demo of one story building in Commons and started demo of elevator shaft
- Continued installing hangers and pipe on 3rd floor A/B hallways for dual temp piping
- Continued demo & rewiring fire alarm cable & installing ductwork on floors 2 & 3 A & B hallway

Downers Grove North High School

Phase B - Gym, Kitchen, Alley, Multipurpose, and Gymnastics Loft Addition

- Interior MEP rough in ongoing on the 1st Floor – insulation to follow behind
- Priming of Gym & Cafeteria/Kitchen CMU walls has been complete
- Framing complete in Kitchen & Alleyway
- Completed drywall on 2nd floor and started in Kitchen & Cafeteria Areas
- Interior demo for miscellaneous MEP penetrations are currently underway
- Lu/La lift scheduled to be delivered in 2 weeks. MEP rough in currently underway in Basement
- Temporary roofing has been removed in the alleyway for the tie-in work to begin.

360° Pictures: Main Gym | Kitchen | Servery | Multi-Purpose Room | Gymnastics Room

Downers Grove North High School

Phase B - Bleachers & Squad Rooms

- All bleacher framing, walkways, flooring, & perimeter fencing have been installed
- Press box was successfully set
- Bleacher benching and interior railing to be complete by end of week
- Underground plumbing and electrical utility work is set to begin next week in order to prepare for the incoming slab on grade pour the following week

Downers Grove North High School

Phase C - Cafeteria, Culinary Arts, Commons, and Southeast Addition

- Interior detail & exterior walls demo have been complete. Interior demo for misc MEP penetrations currently underway in the Library
- Stairwells demo in SE Addition and Purple gym is underway
- Demoed entryway into the courtyard & made penetrations along curtain wall for incoming work
- Clearing and excavation of the courtyard is currently in progress
- Demo of the interior courtyard elevator shaft to begin next week
- Layout for framing has begun on the 2nd and 3rd floors to prep for the incoming MEP rough-ins
- MEP overhead work has begun in the Cafeteria area – flooring infills with lintels and decking have been made to accommodate the new building layout

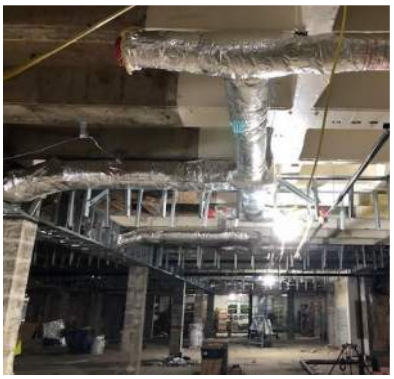

360° Pictures: Commons
